
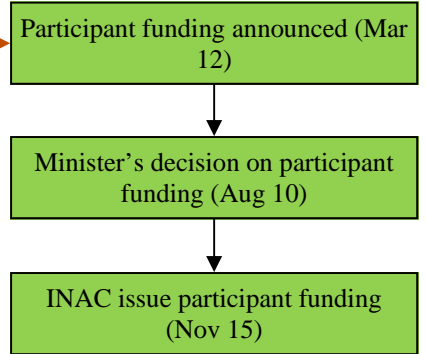


# NIRB's Review Process Map and Anticipated Timeline for the Kiggavik Project<sup>1</sup> (February 6, 2013)

NIRB
Proponent

- Mar 2, 2010
- Mar 12, 2010
- Apr 25 - May 10, 2010
- Nov 15, 2010
- Feb 9, 2011
- Mar 21, 2011
- Mar 22 - Mar 24, 2011
- May 3, 2011
- Dec 20, 2011
- Apr 25, 2012 Resubmission
- May 4, 2012
- May 22 - May 30, 2012
- Jun 29, 2012
- July 13, 2012
- Jan 31, 2013
- Feb 6, 2013
- Apr 8, 2013
- May 8, 2013
- May 28-31, 2013
- June 4-6, 2013
- Jul 4, 2013

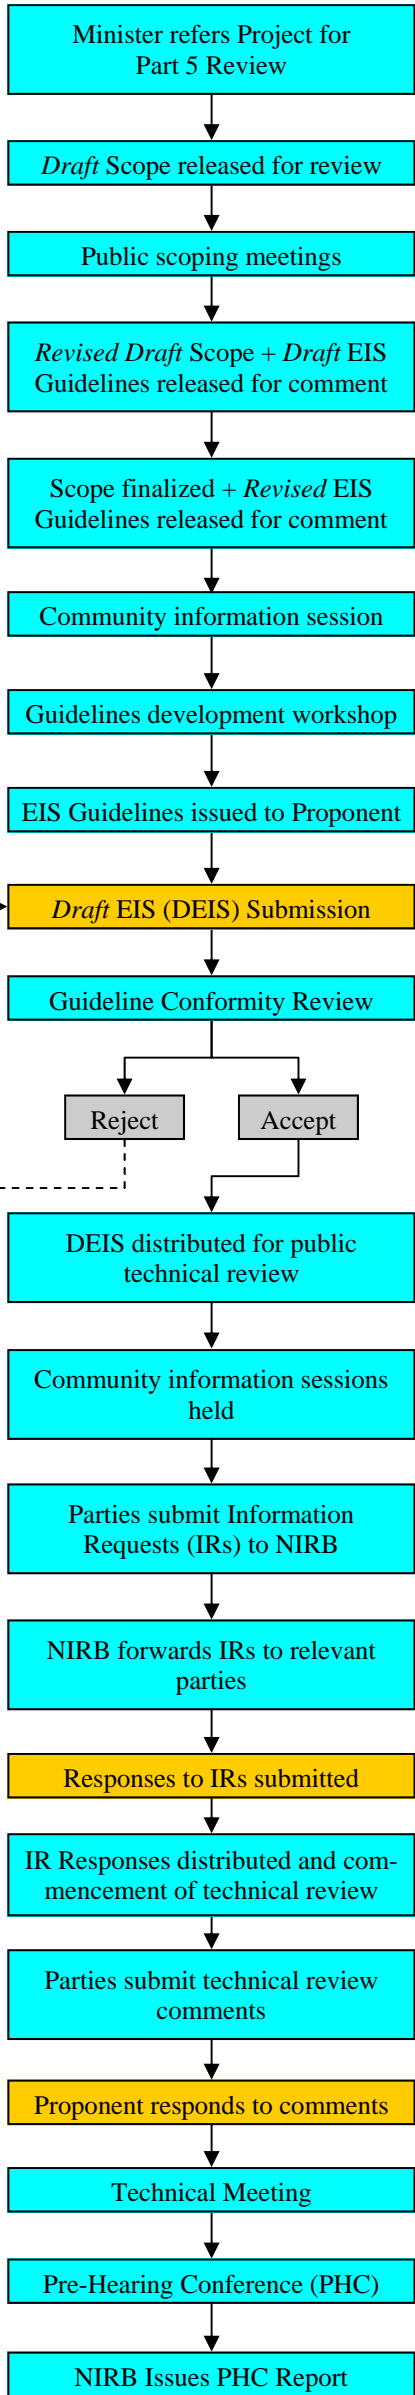


DEIS submitted by the Proponent did not meet the NIRB's conformity determination. The Proponent was asked to resubmit its DEIS on January 18, 2012. Resubmission received April 25, 2012.

The Proponent will develop an FEIS with the issued PHC compliance report based on its own timetable, making the transition to the next stage of the Review Proponent-driven.

# NIRB's Review Process Map and Anticipated Timeline for the Kiggavik Project<sup>1</sup> (February 6, 2013)

NIRB
Proponent

- Continued from previous page -

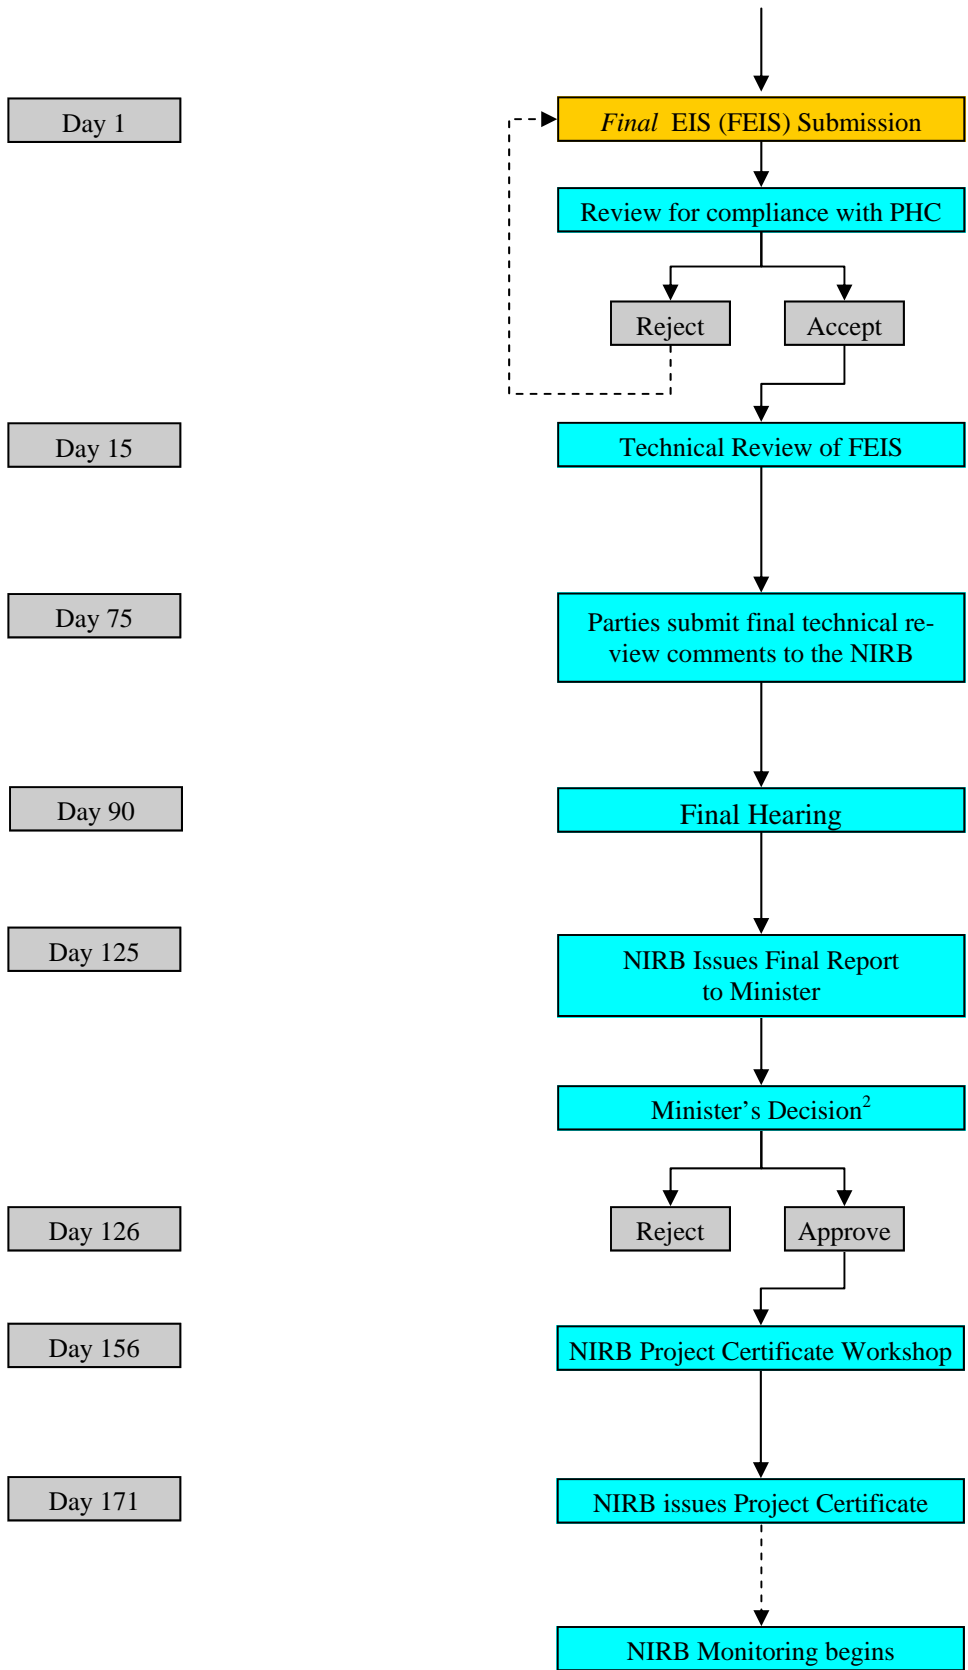

Notes: 1 = Timelines may change based on project-specific circumstances and subject to the NIRB's discretion.  
 2 = The timeline for the Minister's Decision is independent of the NIRB.
